



# LEARIE CONSTANTINE COMMUNITY CENTRE Detailed Programme



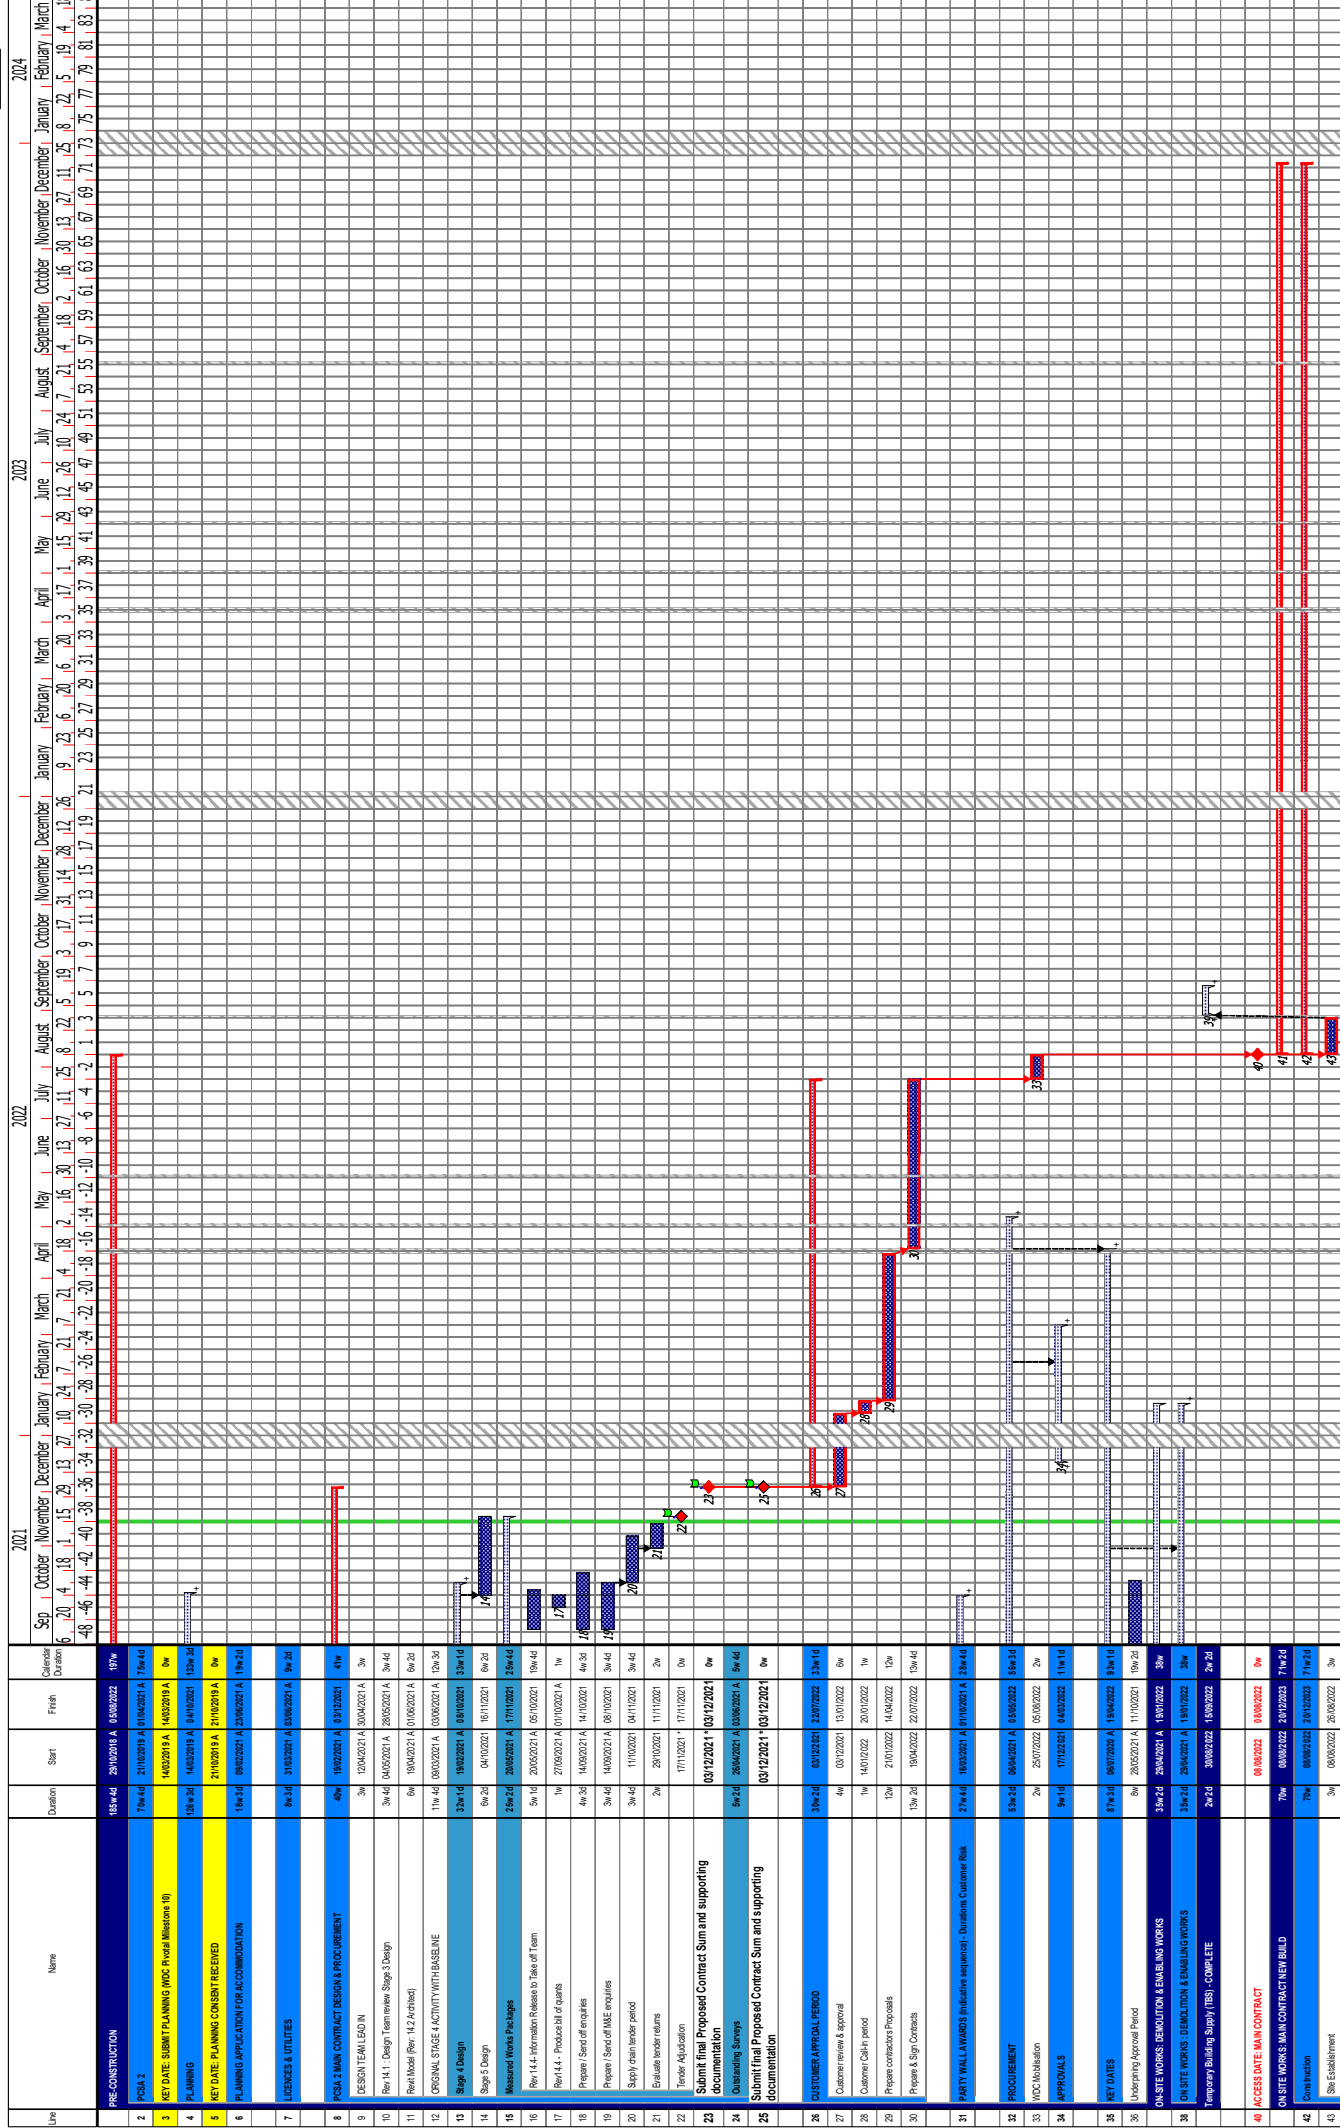


# LEARIE CONSTANTINE COMMUNITY CENTRE Detailed Programme

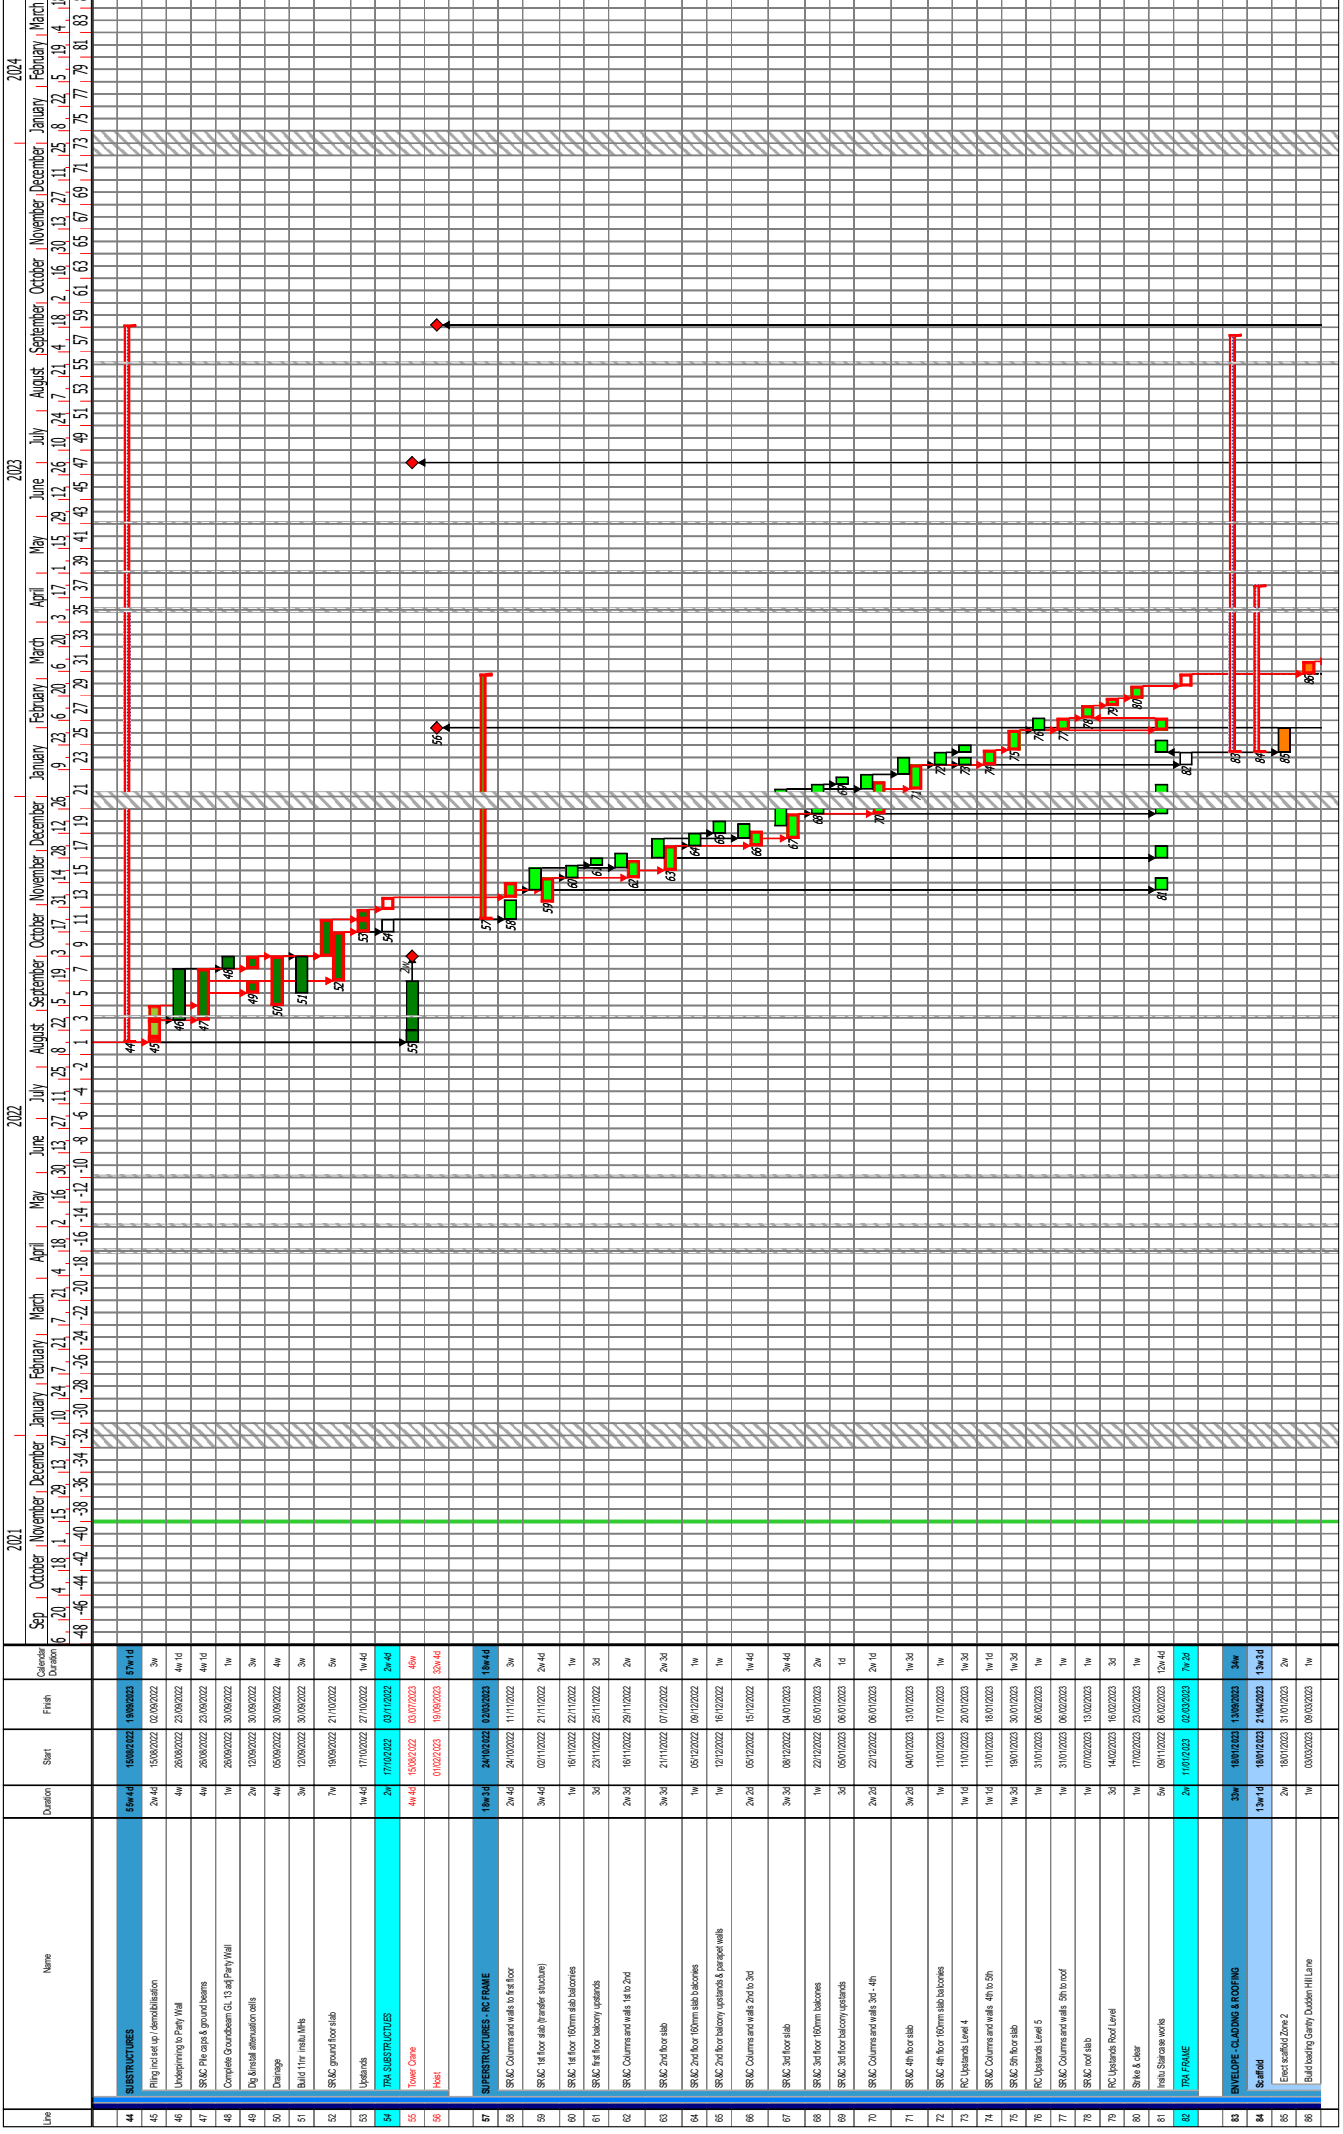


Live	Name	Duration	Start	Finish	Calendar Duration
44	<b>SUBSTRUCTURES</b>	5w 4d	19/09/2021	19/09/2021	57w 1d
45	Piling for tie up / demobilisation	2w 4d	19/09/2021	02/10/2021	3w
46	Underpinning to Party Wall	4w	20/09/2021	12/10/2021	4w 1d
47	S/M/C 2nd floor ground beams	4w	20/09/2021	23/10/2021	4w 1d
48	Complete Groundbeam GL 13.8g Party Wall	1w	20/09/2021	30/09/2021	1w
49	D/B Urethol alternative cells	2w	12/09/2021	30/09/2021	3w
50	Demolish	4w	05/09/2021	30/09/2021	3w
51	Build 11th rebar/tilts	3w	12/09/2021	30/09/2021	3w
52	S/M/C ground floor slab	7w	19/09/2021	21/10/2021	5w
53	Utilities	1w 4d	17/10/2021	27/10/2021	1w 4d
54	<b>7th SUBSTRUCTURES</b>	3w	17/09/2021	03/10/2021	3w 4d
55	<b>Tower Core</b>	4w 4d	15/09/2021	03/10/2021	4w
56	<b>Hot</b>	10/02/2023	19/09/2023	30w 4d	
57	<b>SUPERSTRUCTURES - RC FRAME</b>	1w 4d	24/09/2021	03/10/2021	1w 4d
58	S/M/C Columns and walls to 1st floor	2w 4d	24/09/2021	11/10/2021	3w
59	S/M/C 1st floor slab (transfer structure)	3w 4d	02/10/2021	21/10/2021	2w 4d
60	S/M/C 1st floor 100mm slab balconies	1w	19/10/2021	21/10/2021	1w
61	S/M/C 1st floor balcony upstands	3d	23/10/2021	25/10/2021	3d
62	S/M/C Columns and walls 1st to 2nd	2w 3d	19/10/2021	20/10/2021	2w
63	S/M/C 2nd floor slab	3w 3d	21/10/2021	07/11/2021	2w 3d
64	S/M/C 2nd floor 100mm slab balconies	1w	05/11/2021	19/11/2021	1w
65	S/M/C 2nd floor balcony upstands & parapet walls	1w	12/11/2021	16/11/2021	1w 4d
66	S/M/C Columns and walls 2nd to 3rd	2w 2d	05/11/2021	15/11/2021	1w 4d
67	S/M/C 3rd floor slab	3w 3d	08/11/2021	04/12/2021	3w 4d
68	S/M/C 3rd floor 100mm balconies	1w	22/11/2021	05/12/2021	2w
69	S/M/C 3rd floor balcony upstands	3d	05/12/2021	08/12/2021	1d
70	S/M/C Columns and walls 3rd - 4th	2w 2d	22/11/2021	06/12/2021	2w 1d
71	S/M/C 4th floor slab	3w 2d	04/12/2021	13/01/2022	1w 3d
72	S/M/C 4th floor 100mm slab balconies	1w	11/01/2022	17/01/2022	1w 3d
73	RC Upstands Level 4	1w 1d	11/01/2022	20/01/2022	1w 3d
74	S/M/C Columns and walls 4th to 5th	1w 1d	11/01/2022	18/01/2022	1w 1d
75	S/M/C 5th floor slab	1w 3d	19/01/2022	30/01/2022	1w 3d
76	RC Upstands Level 5	1w	31/01/2022	06/02/2022	3d
77	S/M/C Columns and walls 5th to roof	1w	31/01/2022	06/02/2022	1w
78	S/M/C roof slab	1w	07/02/2022	13/02/2022	1w
79	RC Upstands Roof Level	3d	14/02/2022	16/02/2022	3d
80	Steel & cladding	1w	17/02/2022	23/02/2022	1w
81	Install staircase works	5w	09/11/2021	06/02/2022	12w 4d
82	<b>7th FRAME</b>	2w	11/01/2022	02/02/2022	7w 2d
83	<b>ENVELOPE, CLADDING &amp; ROOFING</b>	3w	19/01/2022	13/02/2022	3w
84	<b>Skaffold</b>	13w 1d	19/01/2022	21/04/2022	13w 1d
85	Erect scaffold Zone 2	2w	19/01/2022	31/01/2022	2w
86	Build back by Cherry Duden Hill Lane	1w	03/02/2022	09/02/2022	1w

# LEARIE CONSTANTINE COMMUNITY CENTRE Detailed Programme

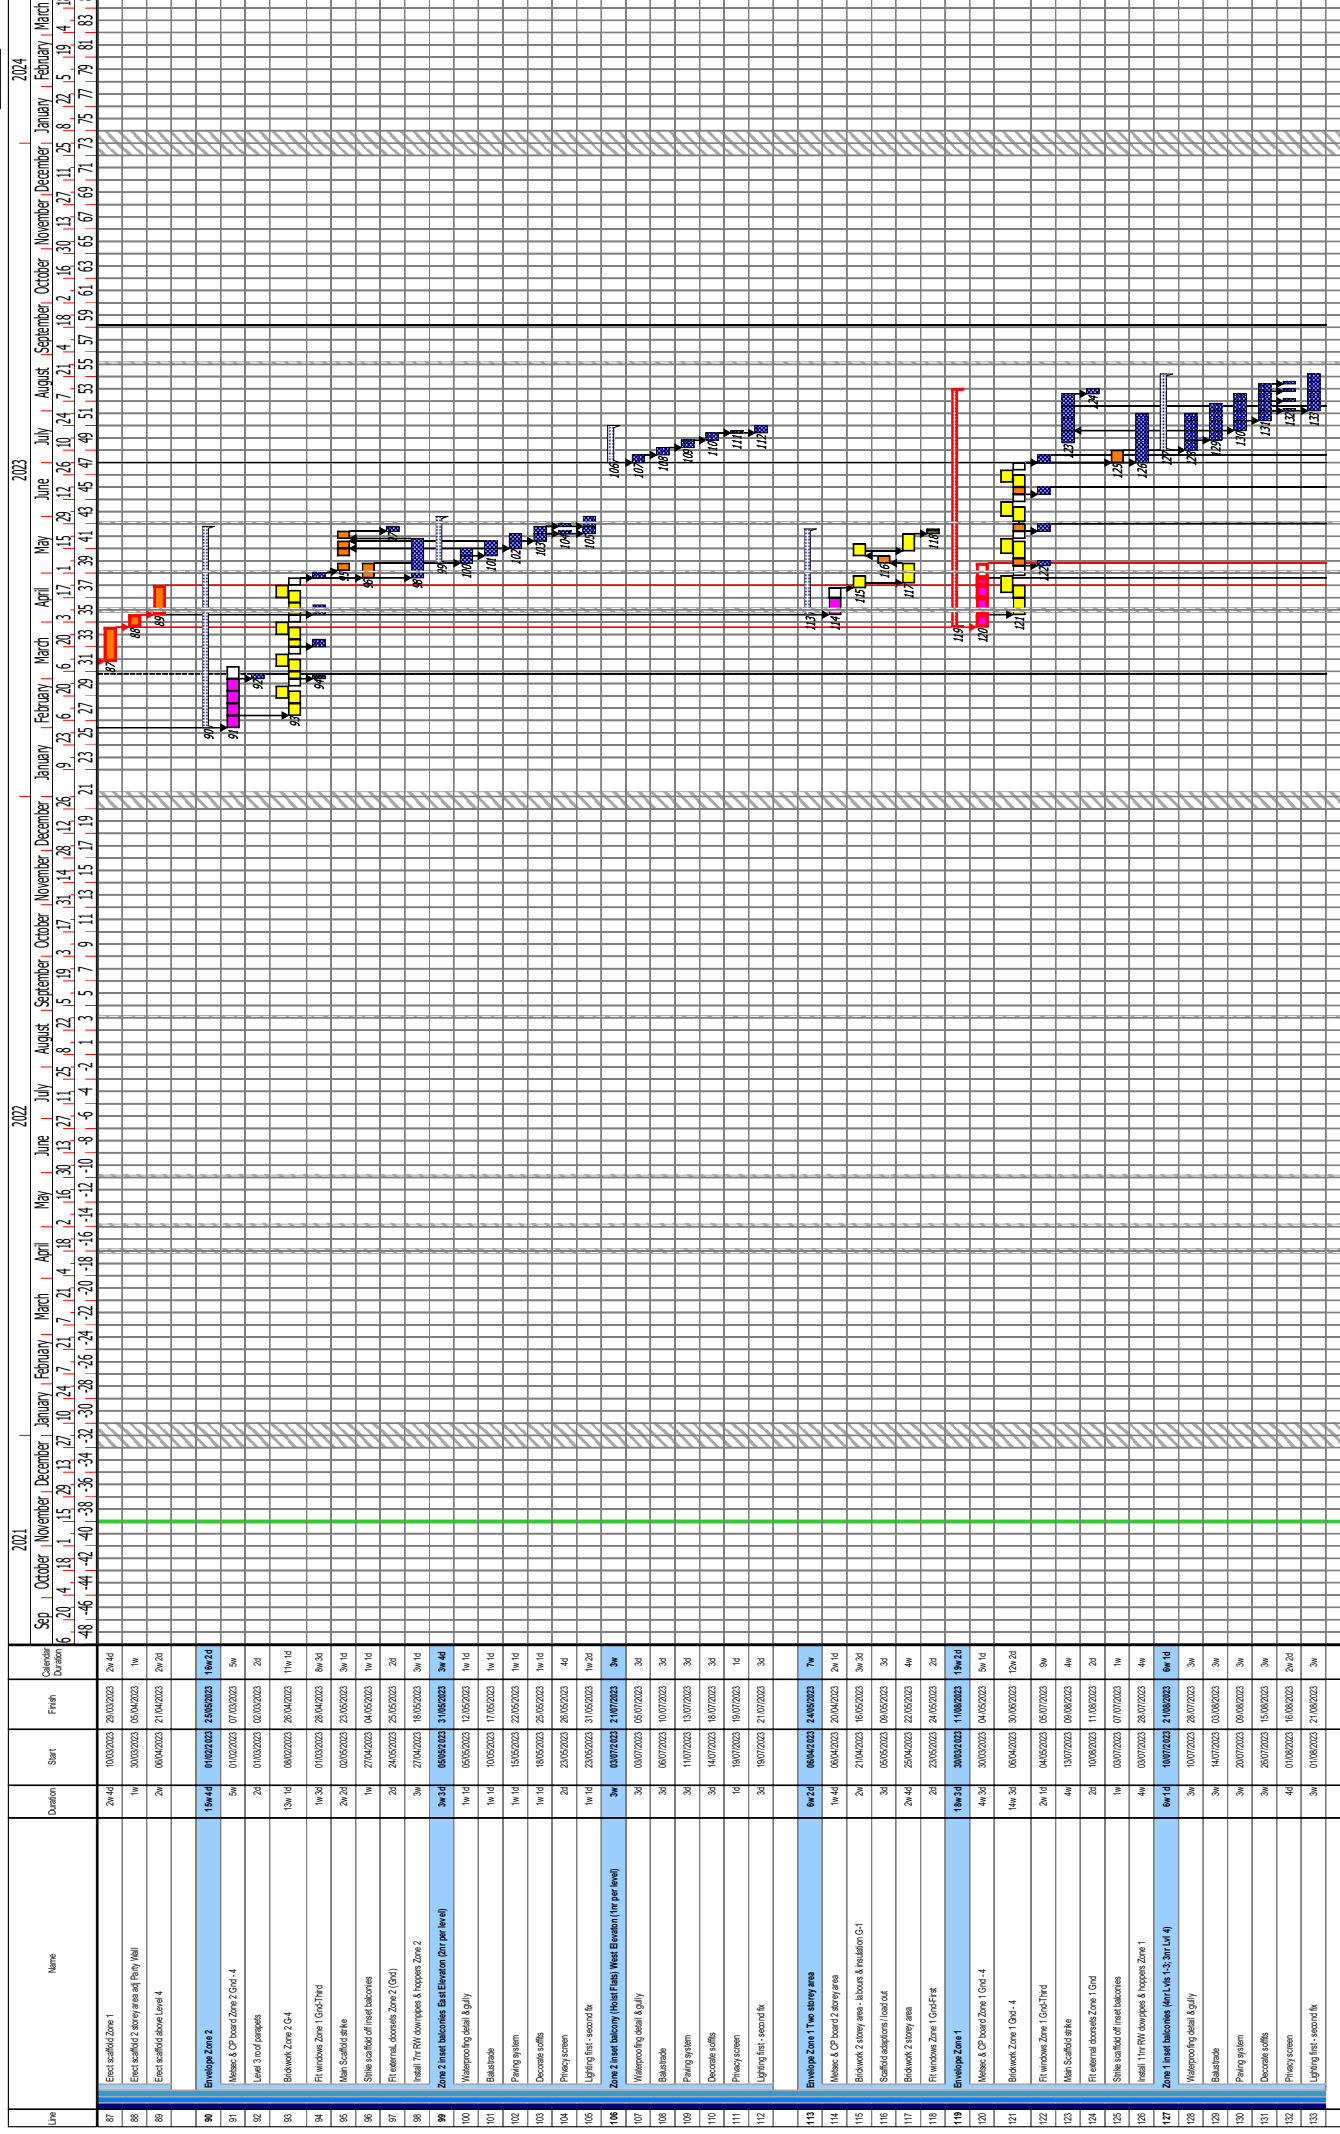





# LEARIE CONSTANTINE COMMUNITY CENTRE Detailed Programme

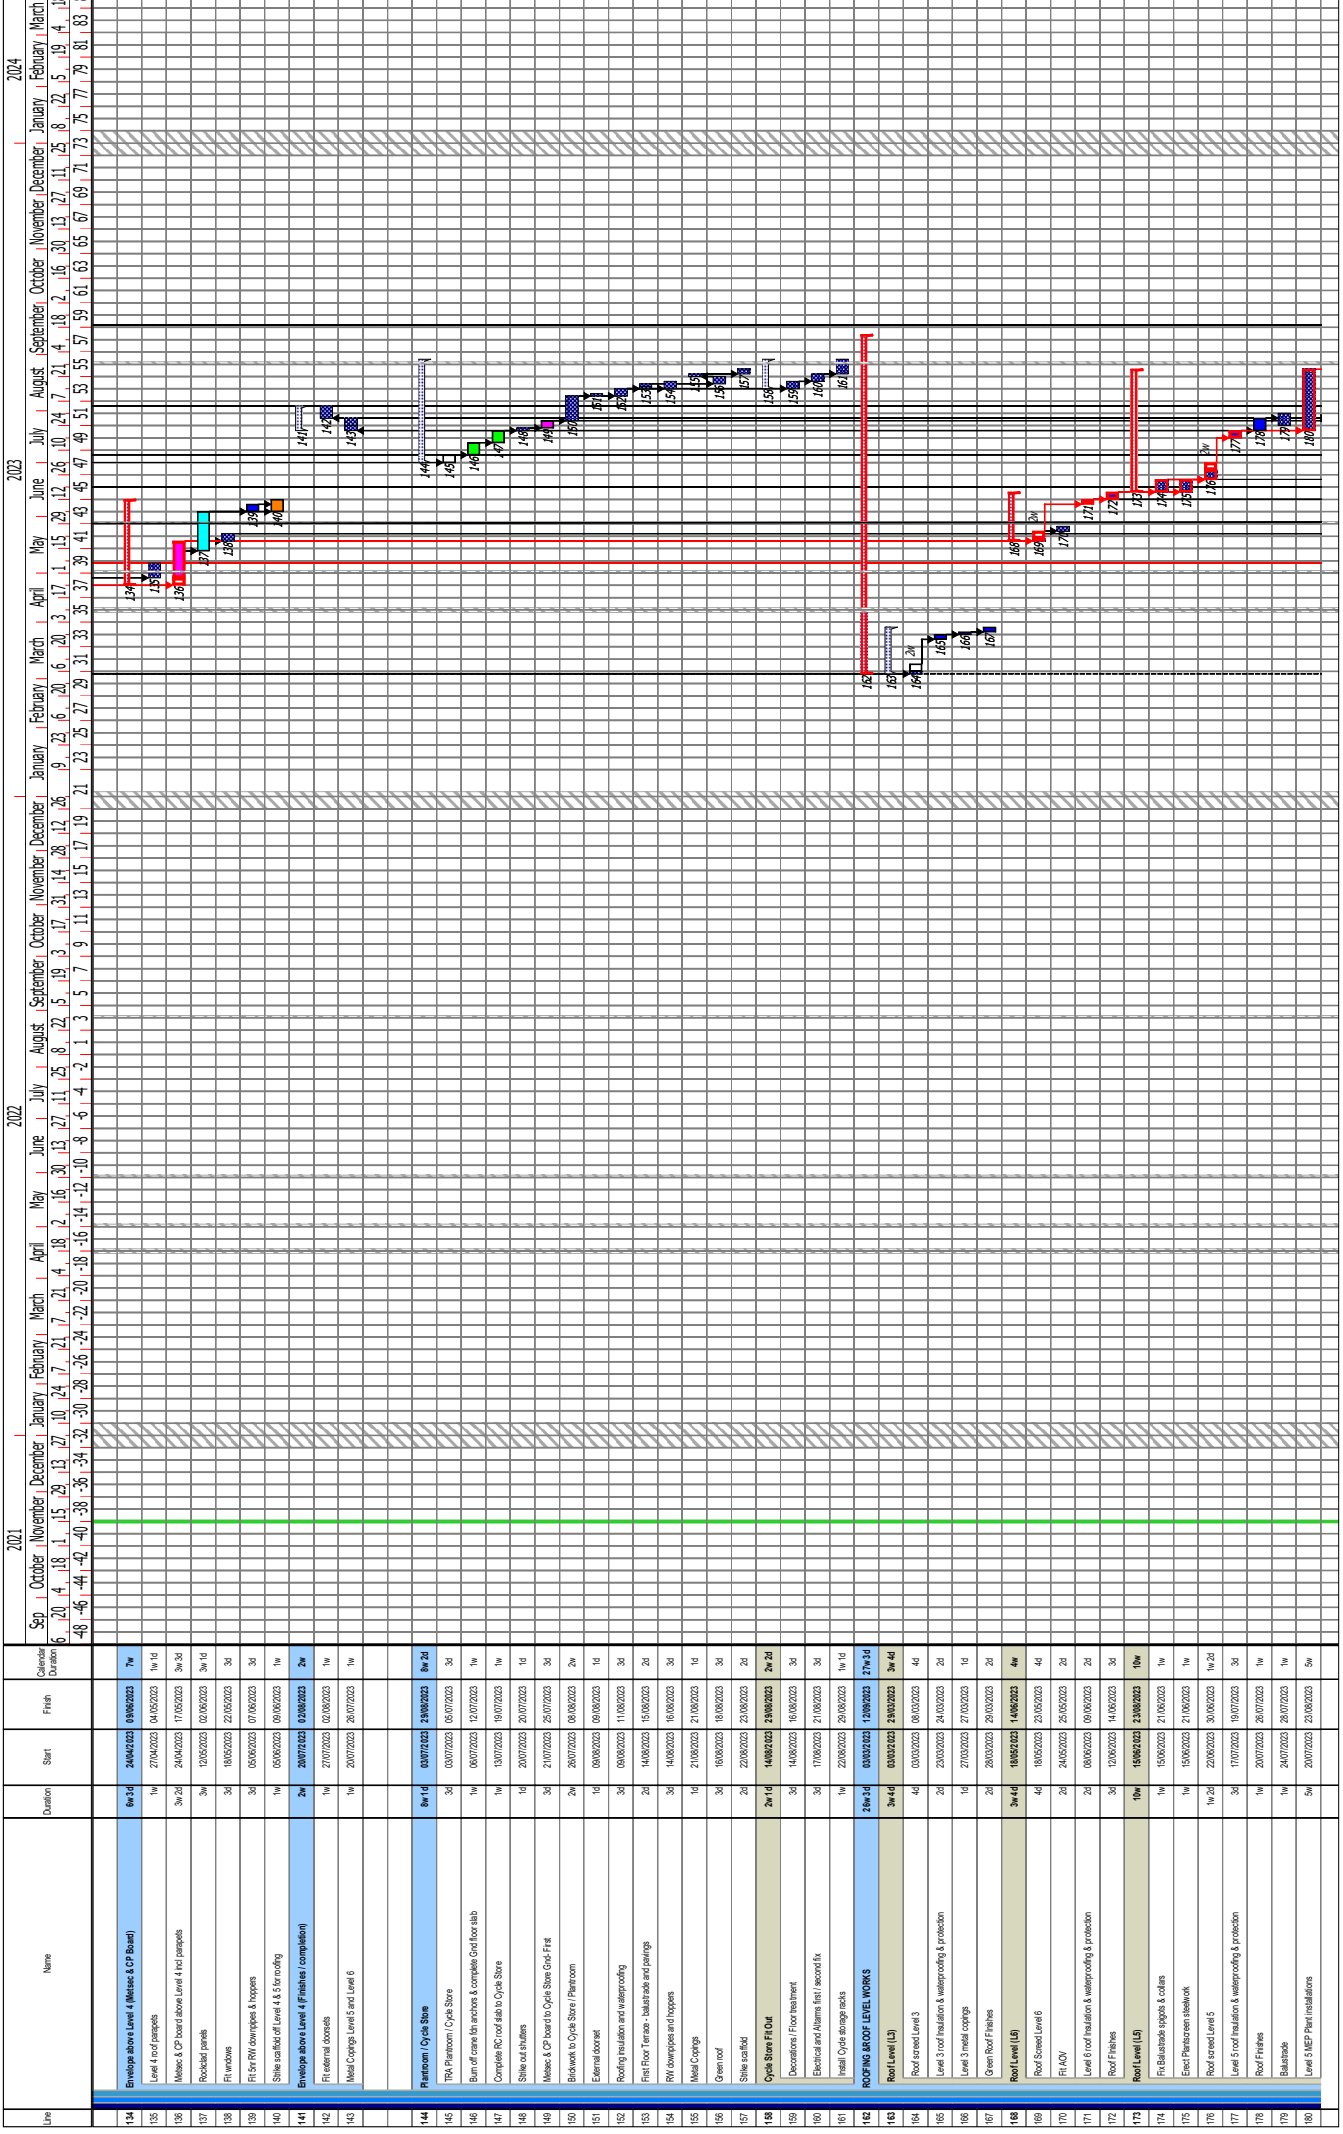


# LEARIE CONSTANTINE COMMUNITY CENTRE Detailed Programme

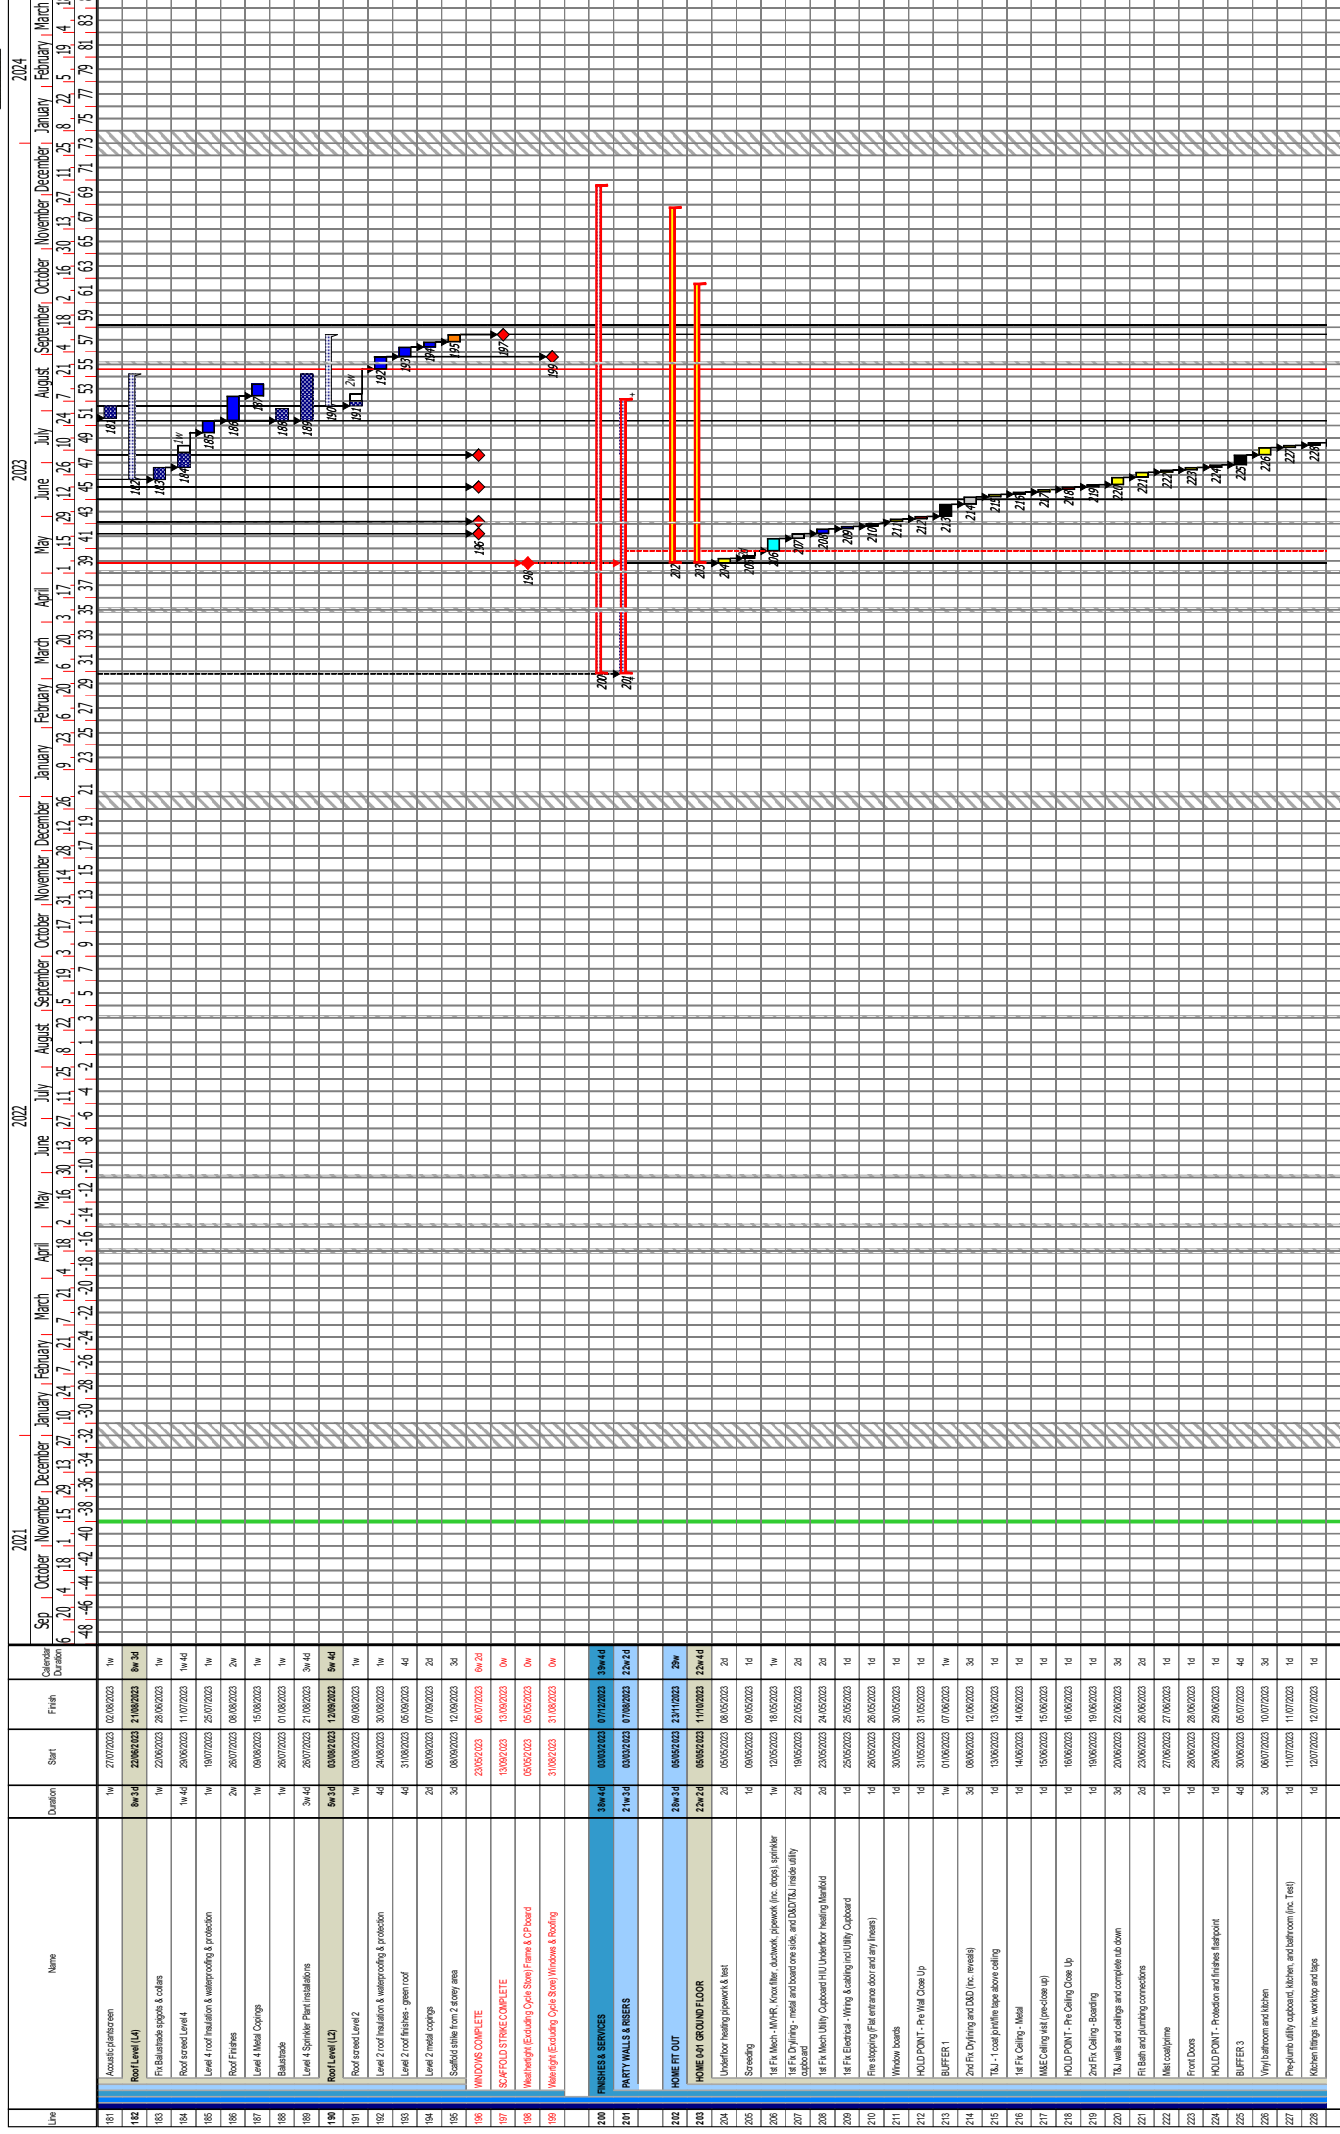

# LEARIE CONSTANTINE COMMUNITY CENTRE Detailed Programme

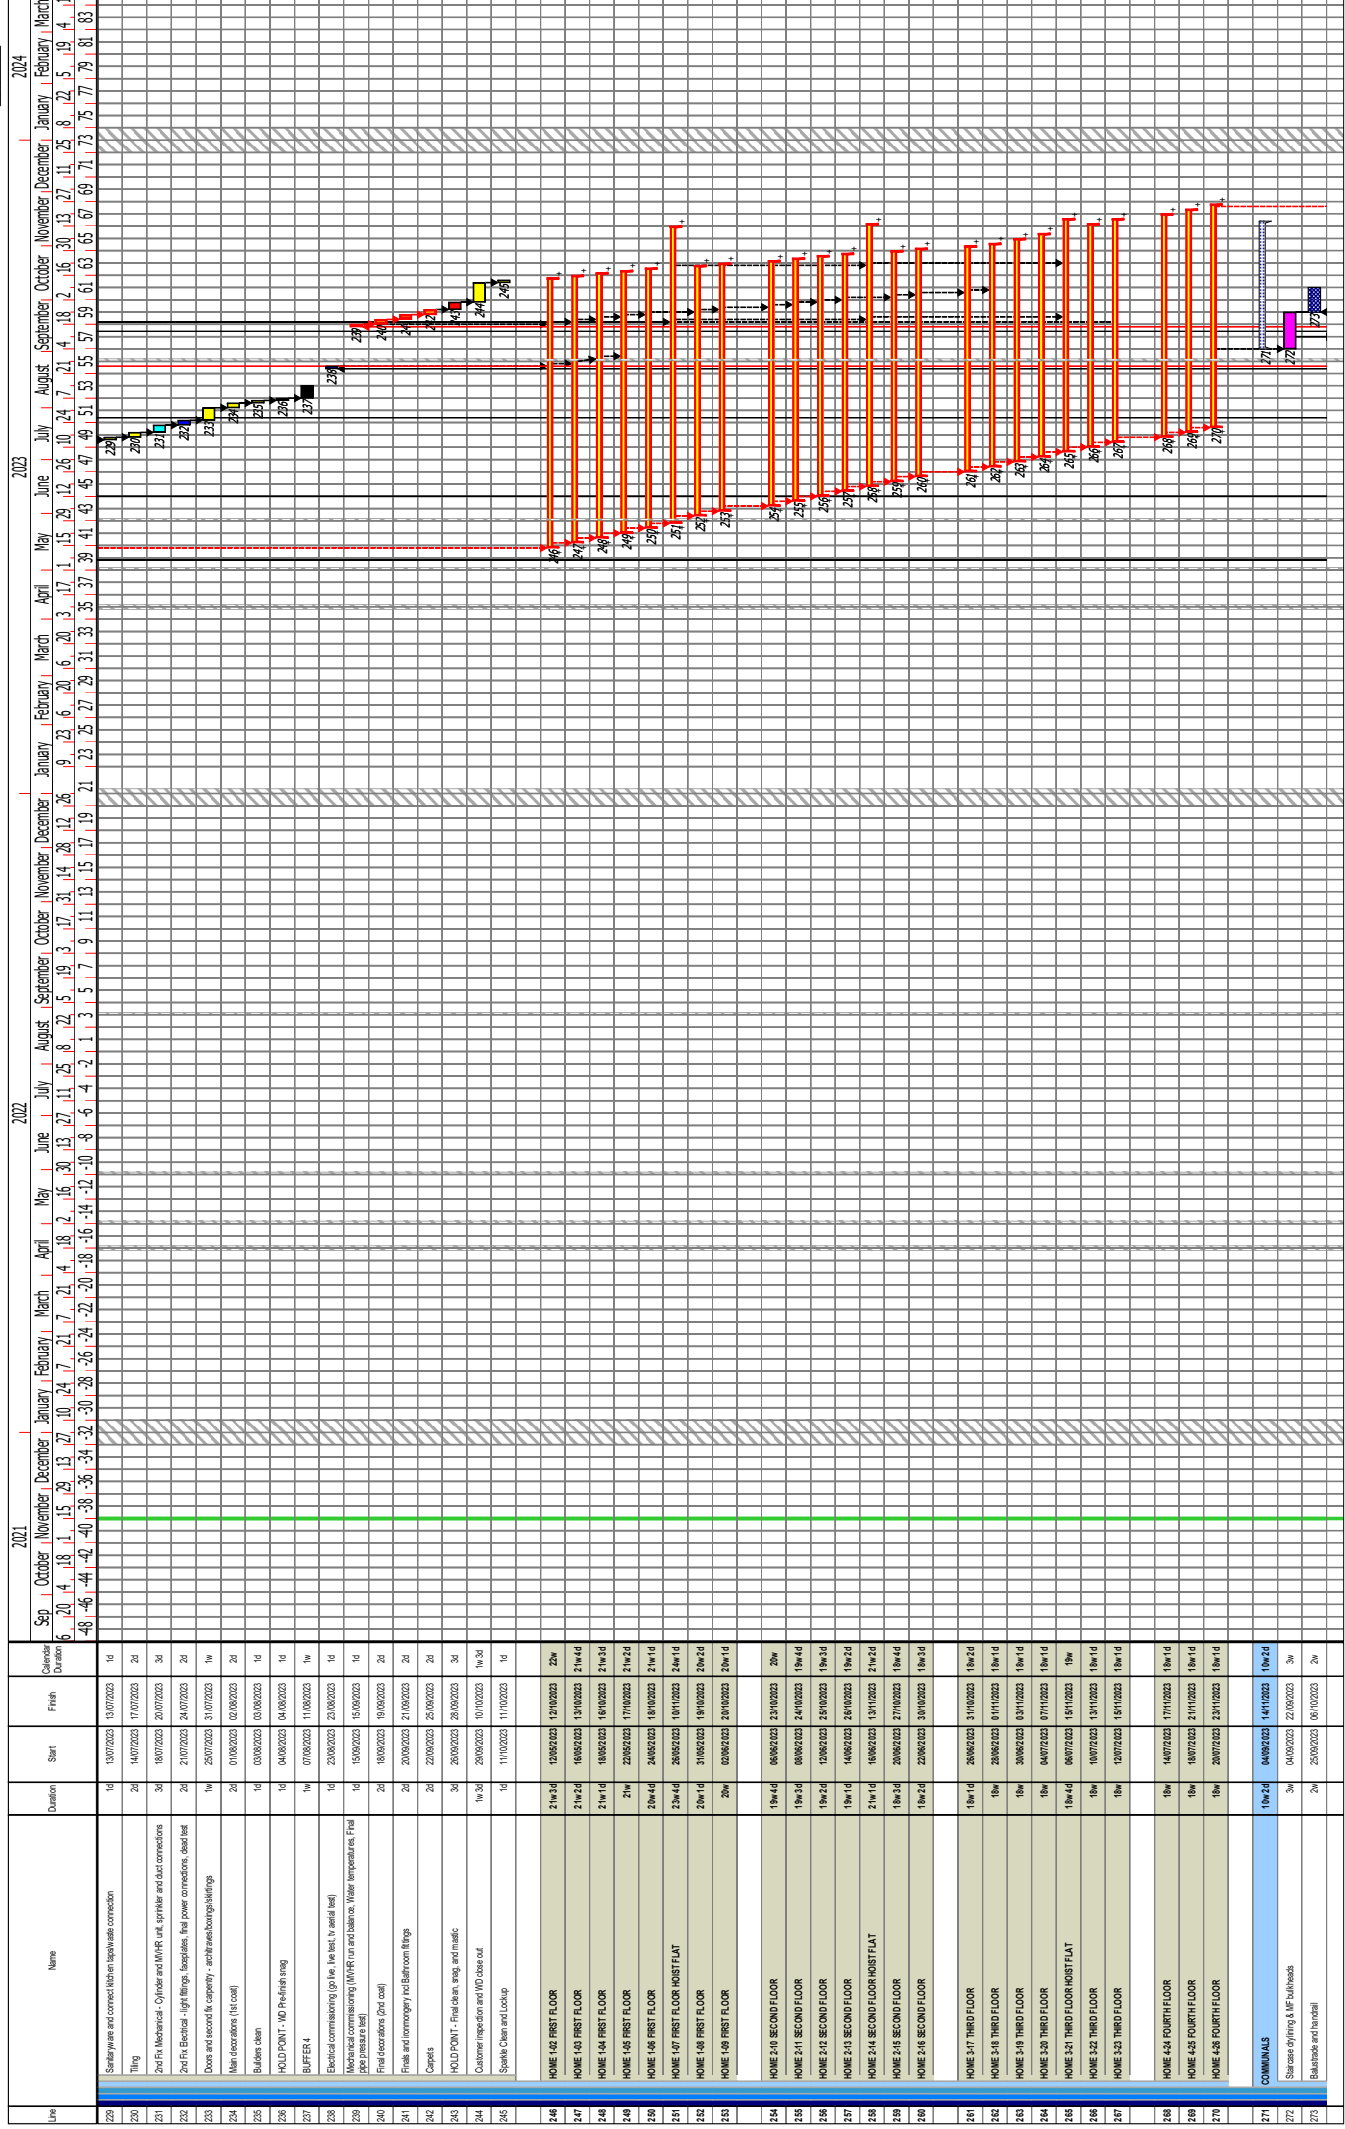

# LEARIE CONSTANTINE COMMUNITY CENTRE Detailed Programme

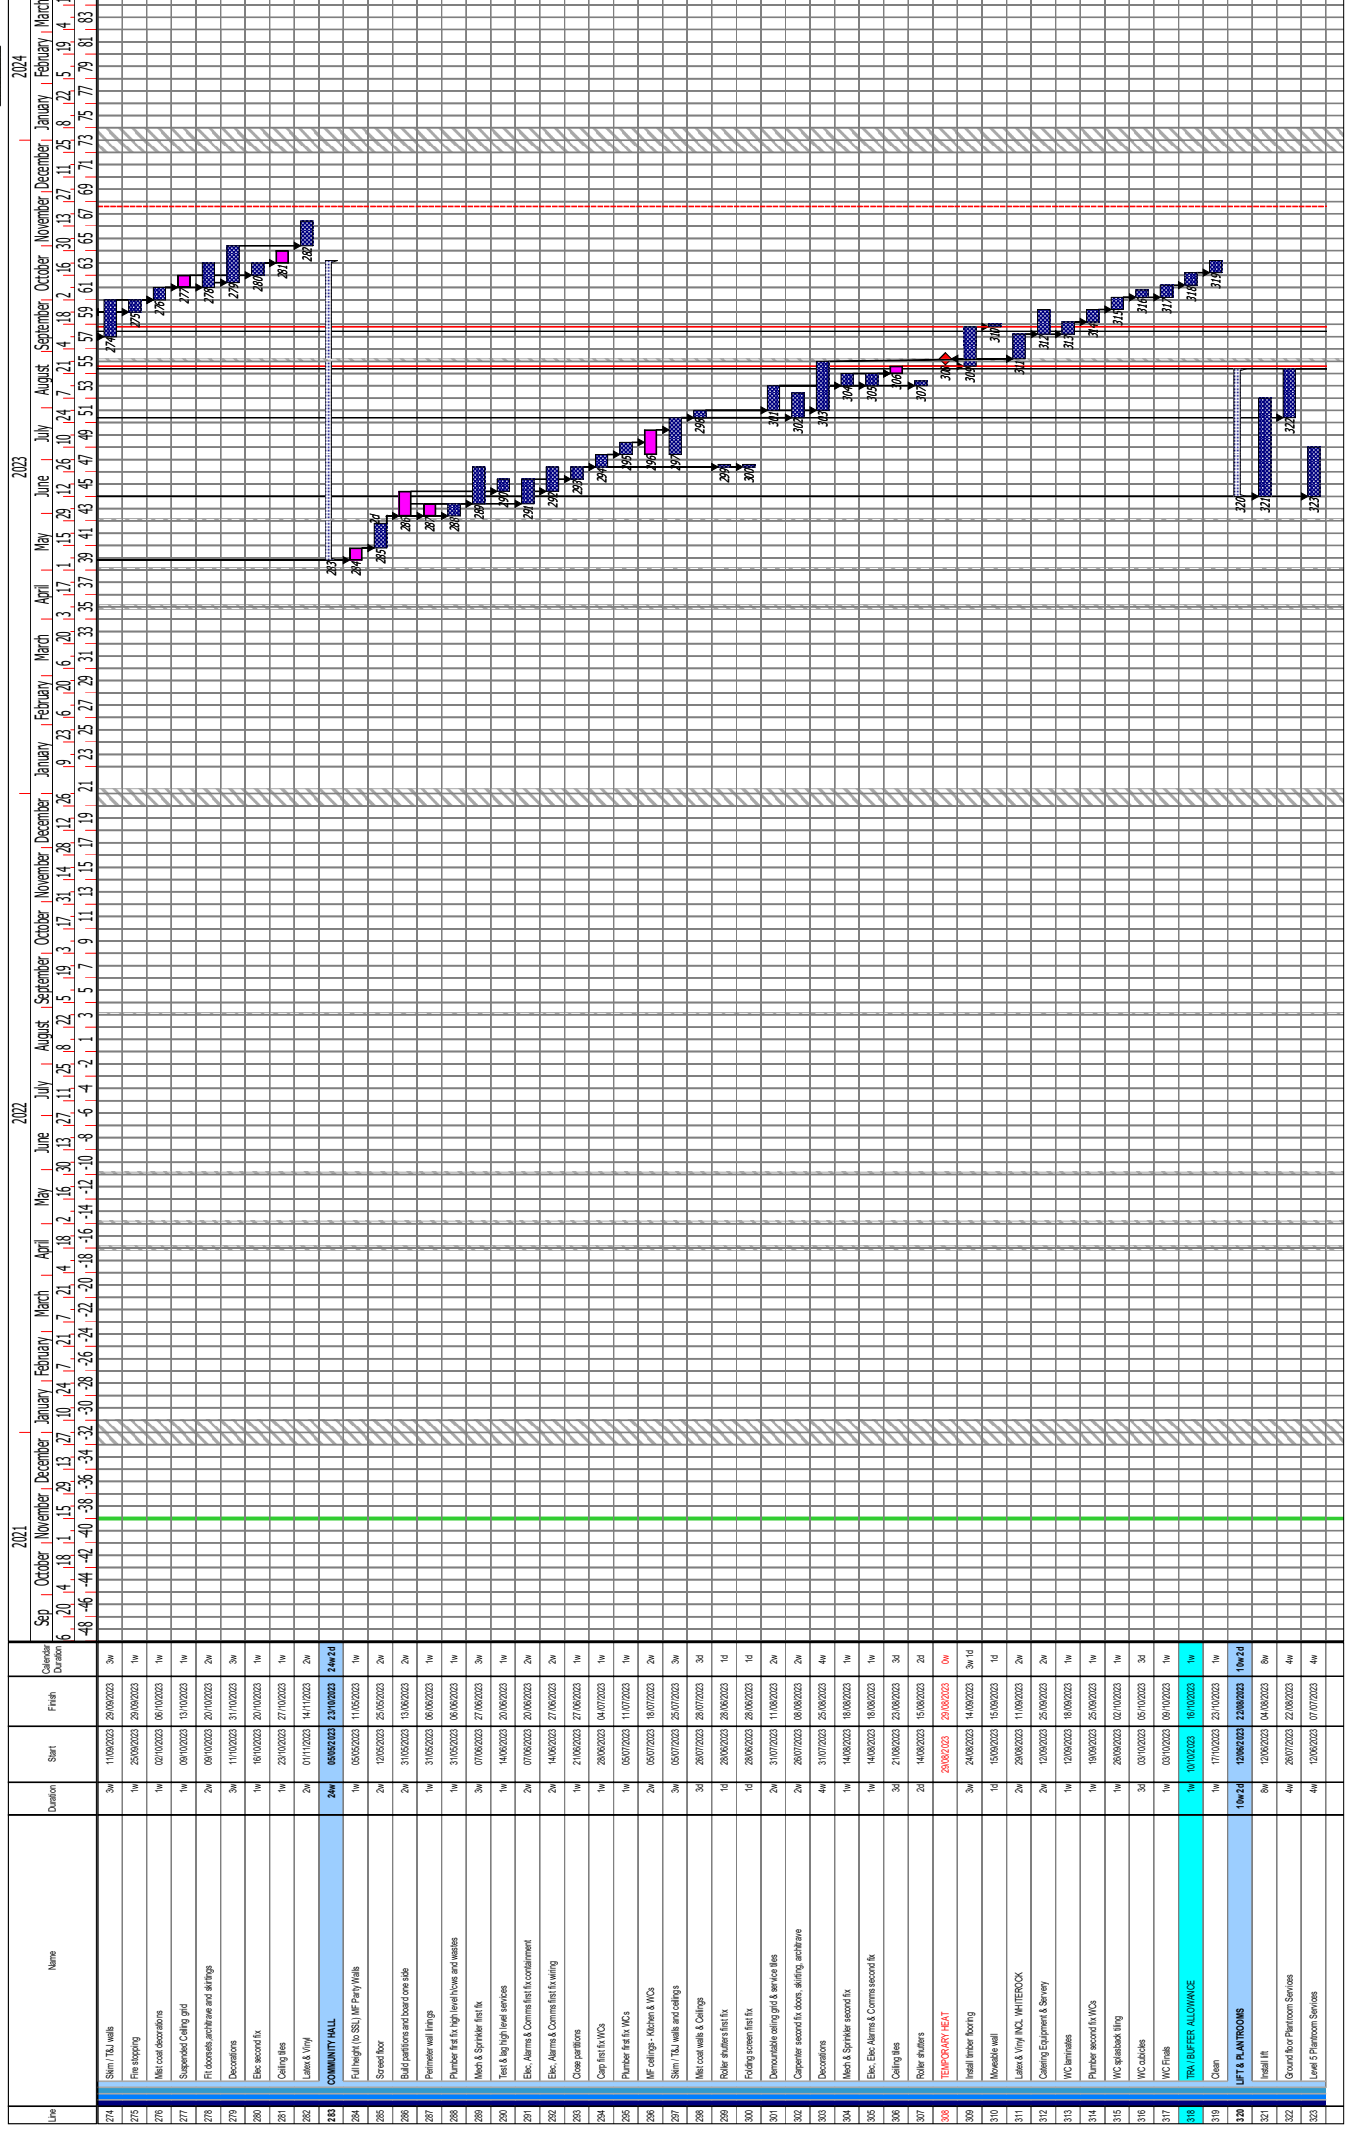



# LEARIE CONSTANTINE COMMUNITY CENTRE Detailed Programme

