










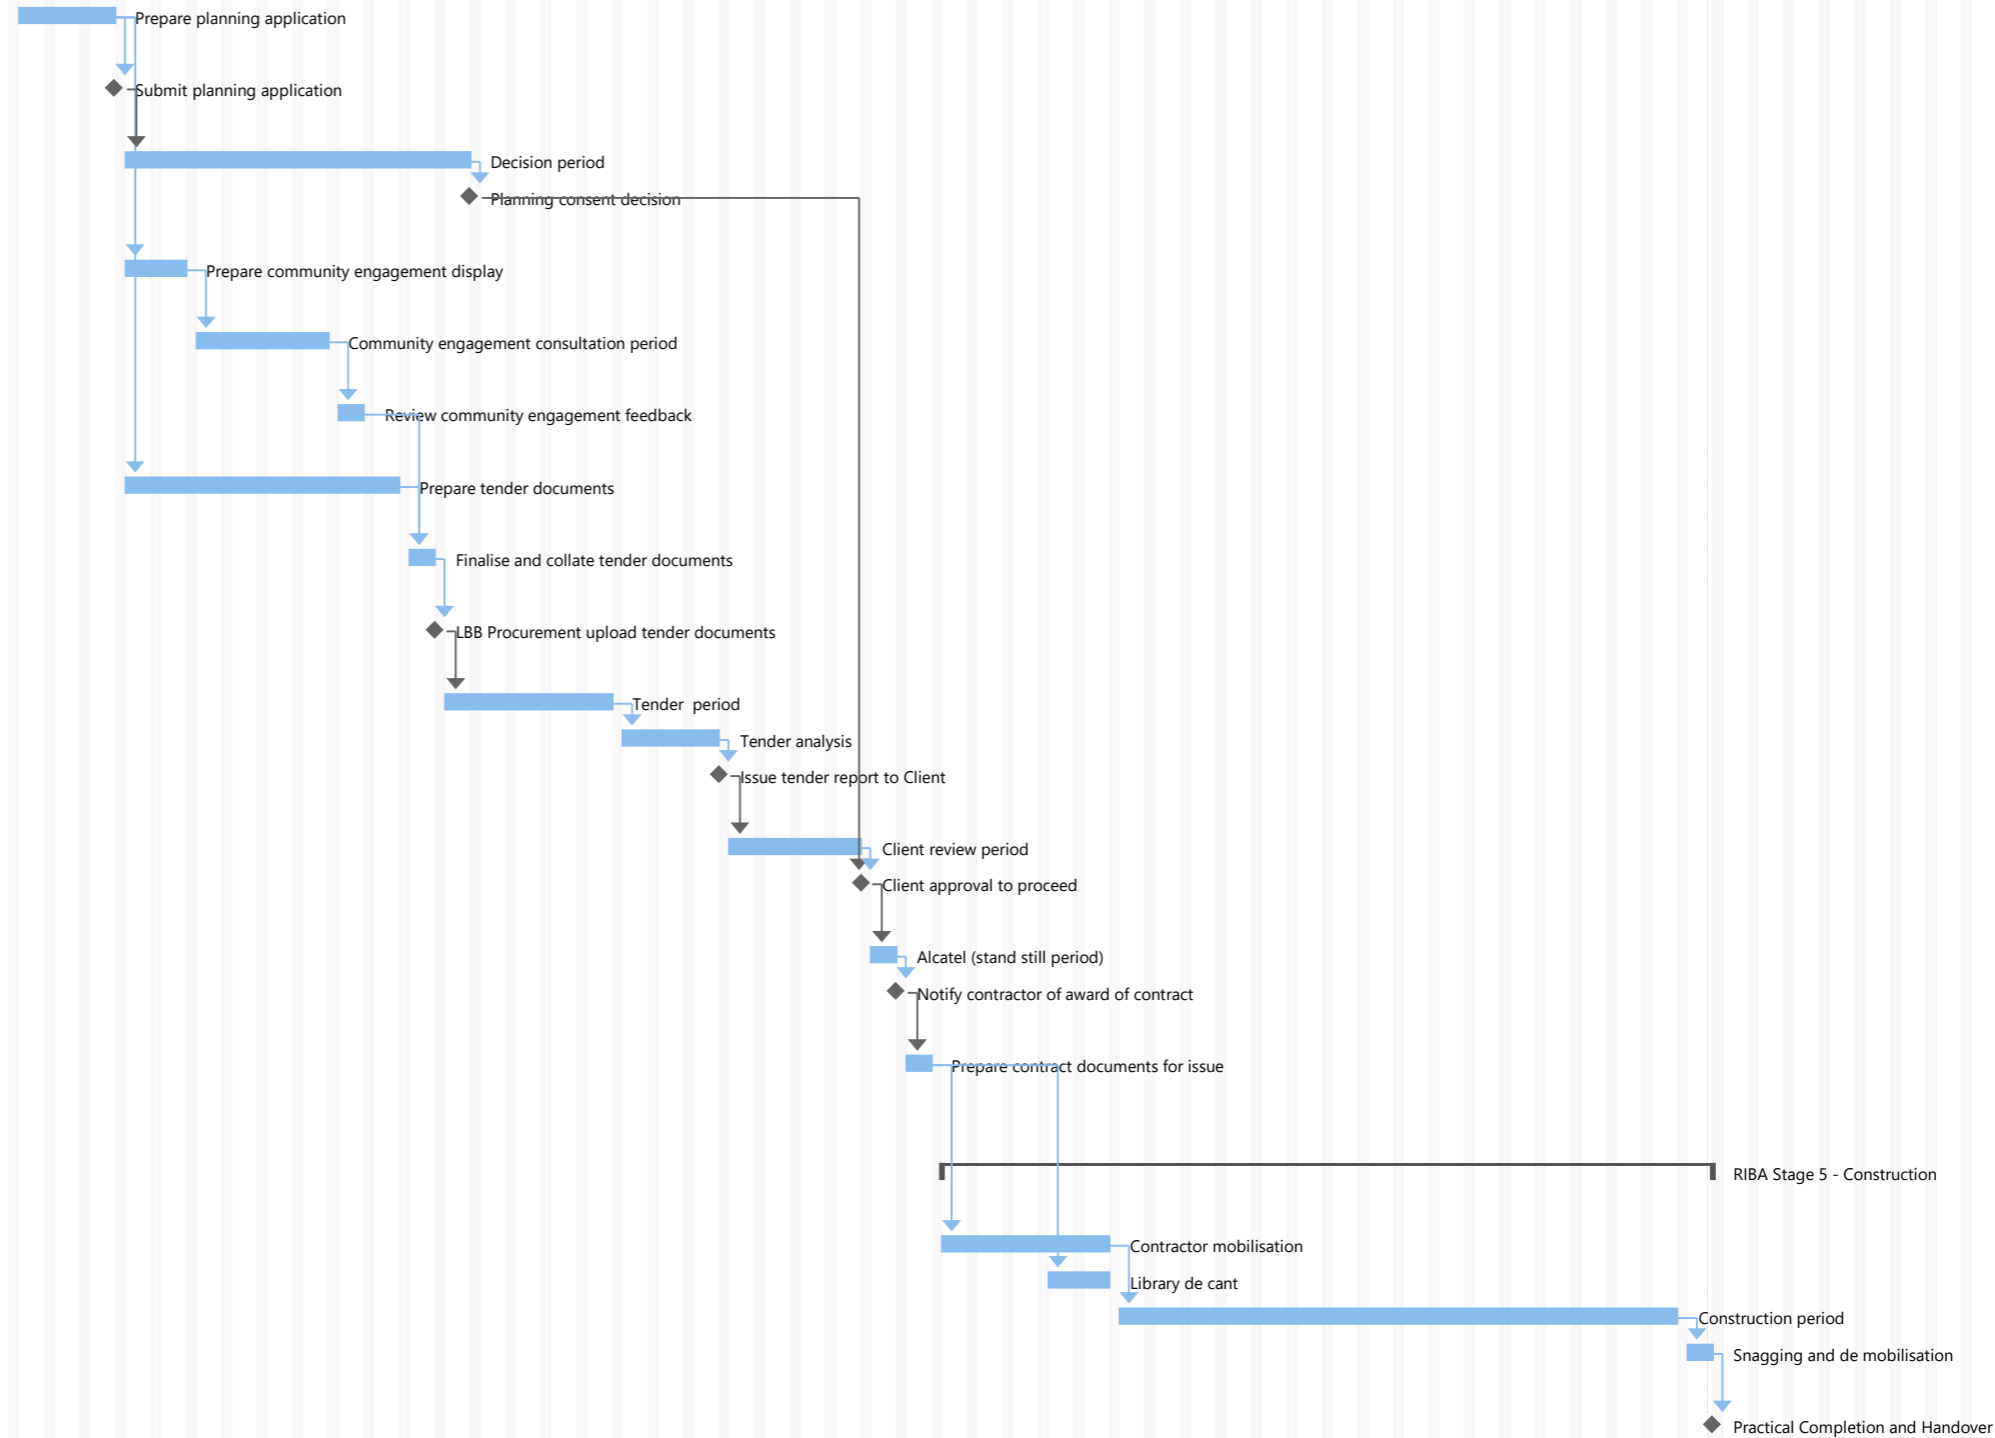







Task Name	Duration	Start	Finish
<b>RIBA Stage 4 -</b>	<b>130 days</b>	<b>Mon 27/03/23</b>	<b>Fri 22/09/23</b>
Prepare planning	15 days	Mon 27/03/23	Fri 14/04/23
Submit planning	0 days	Fri 14/04/23	Fri 14/04/23
Decision period	50 days	Mon 17/04/23	Fri 23/06/23
Planning consent	0 days	Fri 23/06/23	Fri 23/06/23
Prepare	10 days	Mon 17/04/23	Fri 28/04/23
Community	20 days	Mon 01/05/23	Fri 26/05/23
Review community	5 days	Mon 29/05/23	Fri 02/06/23
Prepare tender	40 days	Mon 17/04/23	Fri 09/06/23
Finalise and collate	5 days	Mon 12/06/23	Fri 16/06/23
LBB Procurement	0 days	Fri 16/06/23	Fri 16/06/23
Tender period	25 days	Mon 19/06/23	Fri 21/07/23
Tender analysis	15 days	Mon 24/07/23	Fri 11/08/23
Issue tender report	0 days	Fri 11/08/23	Fri 11/08/23
Client review period	20 days	Mon 14/08/23	Fri 08/09/23
Client approval to	0 days	Fri 08/09/23	Fri 08/09/23
Alcatel (stand still pe	5 days	Mon 11/09/23	Fri 15/09/23
Notify contractor	0 days	Fri 15/09/23	Fri 15/09/23
Prepare contract	5 days	Mon 18/09/23	Fri 22/09/23
<b>RIBA Stage 5 -</b>	<b>110 days</b>	<b>Mon 25/09/23</b>	<b>Fri 23/02/24</b>
Contractor mobilisat	25 days	Mon 25/09/23	Fri 27/10/23
Library de cant	10 days	Mon 16/10/23	Fri 27/10/23
Construction period	80 days	Mon 30/10/23	Fri 16/02/24
Snagging and de	5 days	Mon 19/02/24	Fri 23/02/24
Practical	0 days	Fri 23/02/24	Fri 23/02/24



Task		Project Summary		Manual Task		Start-only		Deadline	
Split		Inactive Task		Duration-only		Finish-only		Progress	
Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
Summary		Inactive Summary		Manual Summary		External Milestone	
